



— BUREAU OF —
RECLAMATION


Arkansas Valley Conduit Update

Derek Mickle, AVC Project Manager
Eastern Colorado Area Office

September 9, 2025



1

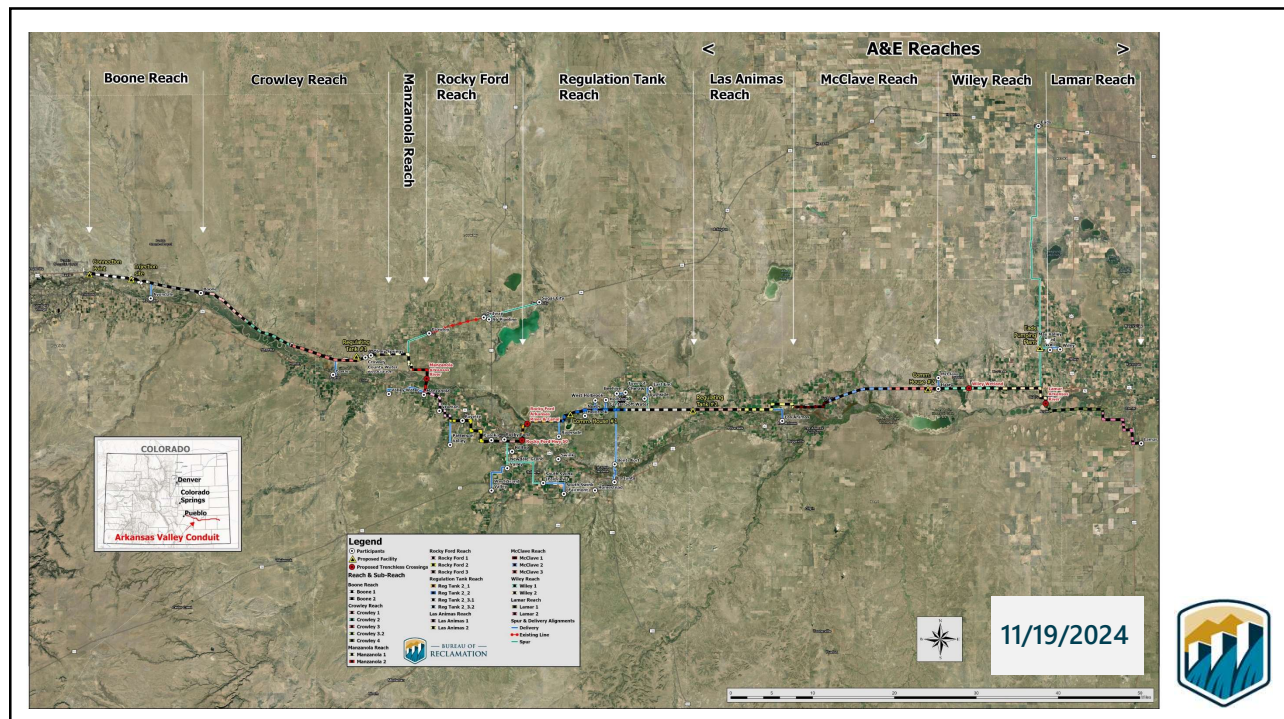

2

Reclamation Staffing

- Recent attrition in key areas
 - Project management
 - Construction services
 - Acquisition contracting
 - Geotechnical drilling
 - Archaeology



3

Future Contracts

- Crowley Reach 1
 - Construction of approximately 5.3 miles of 30-inch potable water transmission pipe and associated improvements. Work includes horizontal directional drilling, bored crossings, and road cuts and restoration.
- Crowley 1 Lands
 - Procurement of temporary/permanent easements
 - Expected this month
- Crowley 1 Construction Award
 - Pending railroad crossing permits
 - Pending signed license agreements
 - Expected Fall/Winter 2026



4

Future Contracts

- Reg Tank 1/Crowley Reaches 2 & 3
 - Construction of a transmission line and water storage tanks to convey water from the Crowley Reach 1 connection point to Crowley Reach 4 connection point located along State Highway 96 approximately 2 miles northeast of the Town of Fowler.
 - Disinfect approximately 5.3 miles of 30-inch transmission piping installed under the Crowley Reach 1 contract, including furnishing and disposal of water.
- Contract 8 A&E Design Award
 - Last 40+ miles of pipe to Lamar
 - Expected this month



5

Current Construction

- Boone Reach 1
 - Successful flush and fill of three sections
 - Successful hydrostatic testing of the full pipe section
- Boone Reach 2
 - Delivery vault installed
 - Waiting on Xcel to relocate gas line before completing pipe
 - Valve assembly to be installed in October 2025.
- Injection Site Phase 1
 - Building ordered; expected January 2026
 - Steel line pipe for foundation ordered



6


Finance and Funding

- 2010 – 2019: \$30 million through regular appropriations.
- 2020: Congress provided a \$28 million appropriation to move the Project into construction.
- 2021-2023: \$31.5 million through regular appropriations.
- 2022: \$60 million from the Infrastructure Investment and Jobs Act.
- 2023: \$100 million from the Infrastructure Investment and Jobs Act.
- 2024: \$90 million from the Infrastructure Investment and Jobs Act + \$10 million appropriations.
- 2025: \$250 million from the Infrastructure Investment and Jobs Act + \$13 million appropriations.
- **Total funded through 2025: \$613 million.**
- **Total estimated federal cost (2023): \$1.3 billion**

Total funding to date brings construction through Manzanola Reach 1, where 9 of 39 communities are served. Total population served is approximately 8,000. Total communities under CDPHE enforcement orders served is 2/18.



7



8
